



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



Joy Cheung
Caltrans
Senior Transportation Engineer



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS





23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS


Stage Construction

- Stage 1 – June 2014 (A) to April 2015 (A)
 - Relocate Lisbon Ave on-ramp to 29th Avenue
 - Construct majority of sound wall
- Stage 2 – April 2015 (A) to May 2017 (A)
 - Reconstruct 29th Ave overcrossing
- Stage 3 – July 2017 (A) to November 2018
 - Construct 29th Ave northbound off ramp structure and roundabout
- Stage 4 – June 2017 (A) to October 2018
 - Reconstruct 23rd Ave overcrossing
 - Maintaining EB Traffic on Southerly Structure
- Stage 5 – October 2018 to January 2019
 - Open New 23rd Ave OC and Demo Southerly Structure
 - Reconstruct 23rd Ave northbound off ramp
 - Complete sound wall construction

Dates subject to change



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

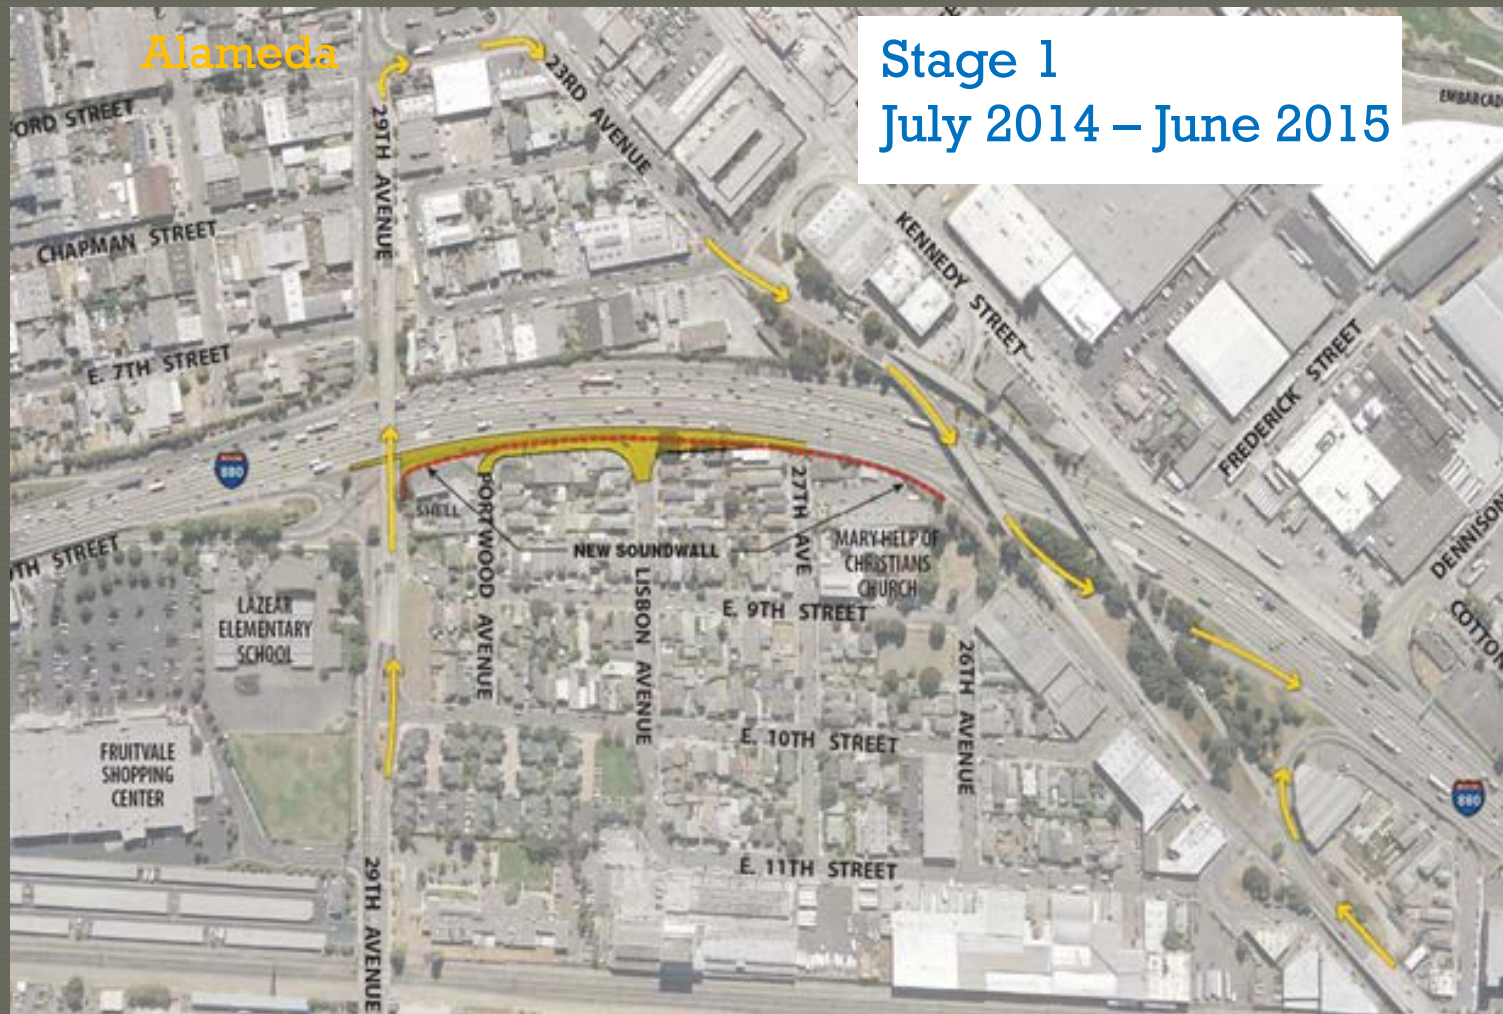




23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS





23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

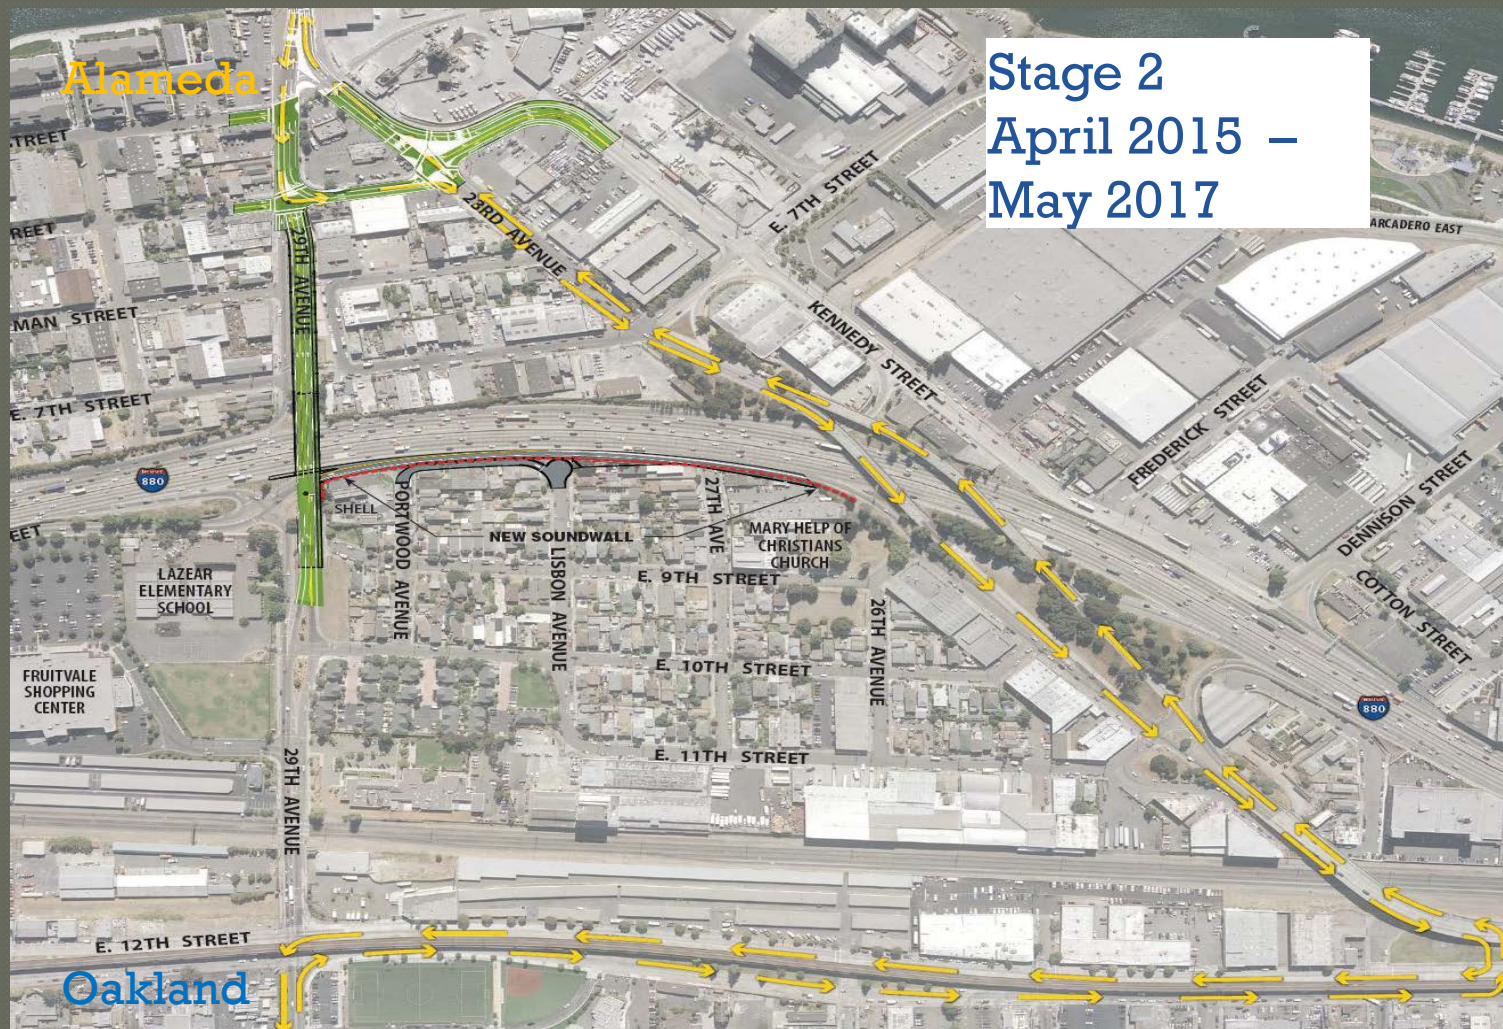



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS




© 2017 California Department of Transportation. All Rights Reserved.




23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

Stage 3
July 2017 to
November 2018

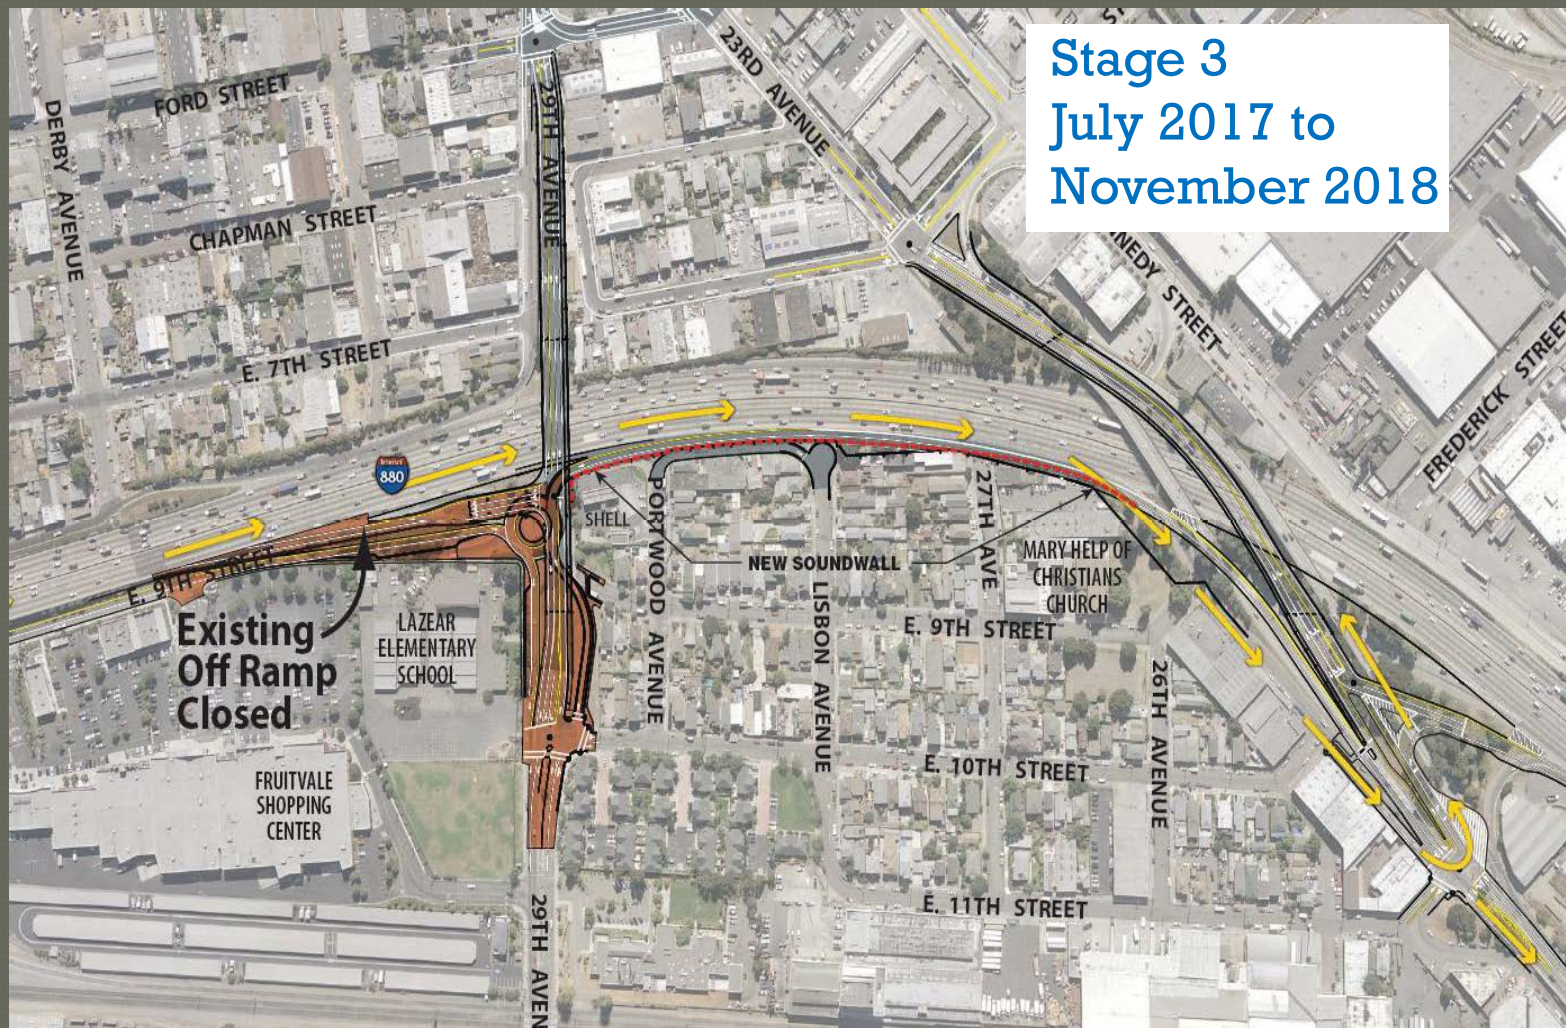




23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

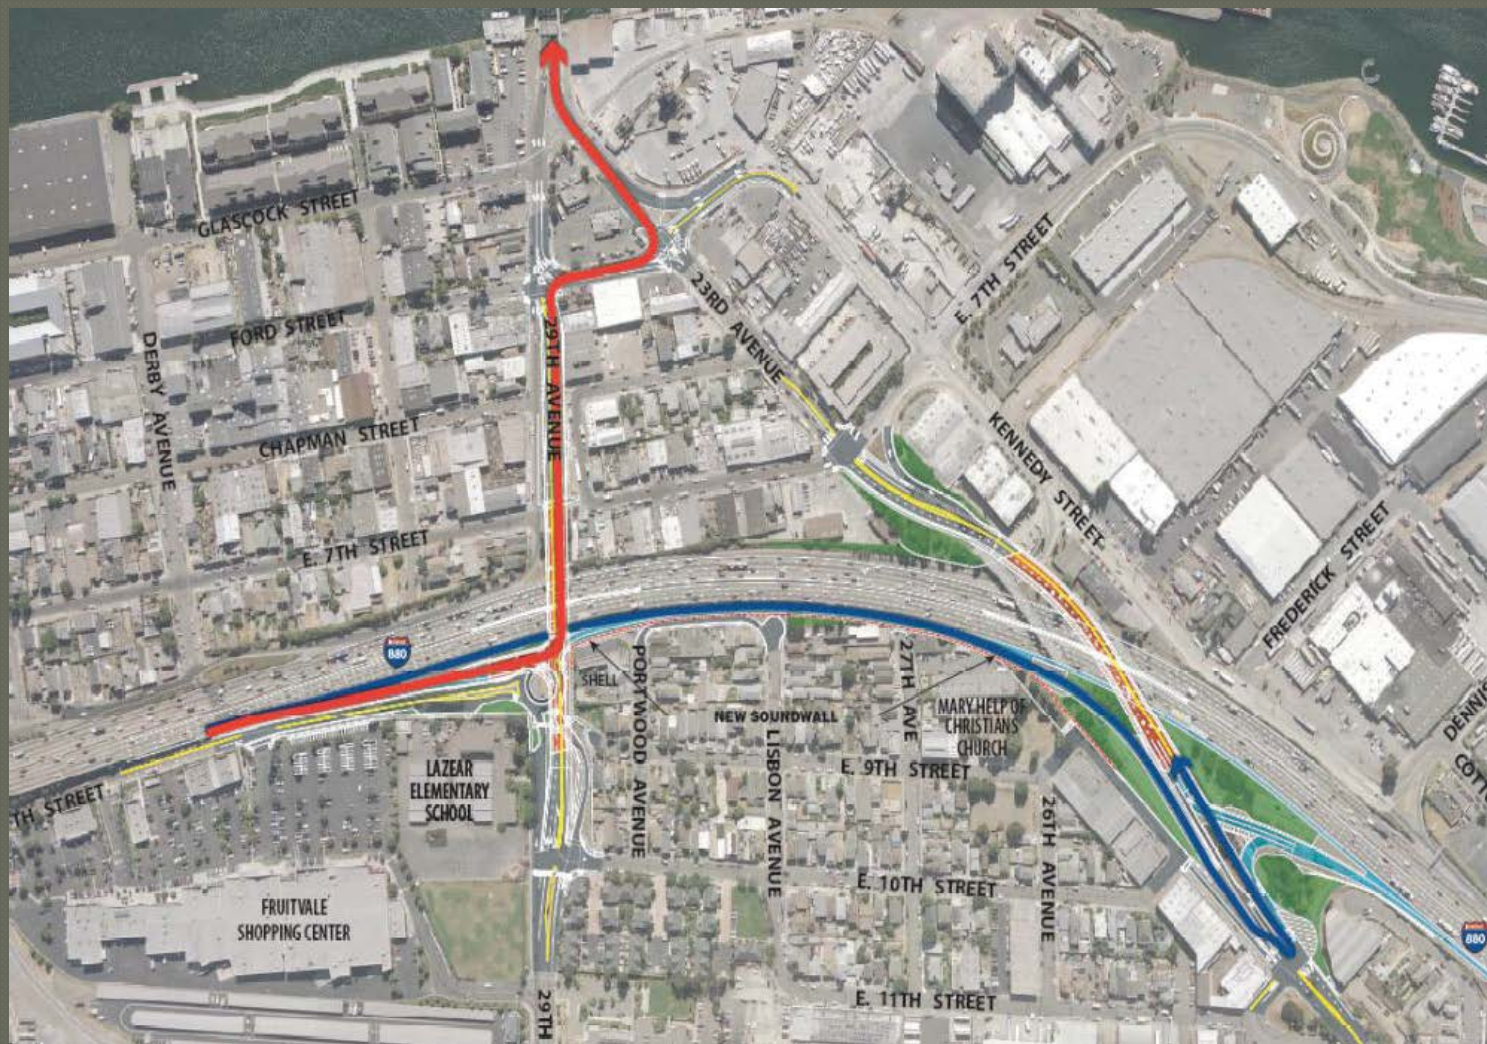

23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



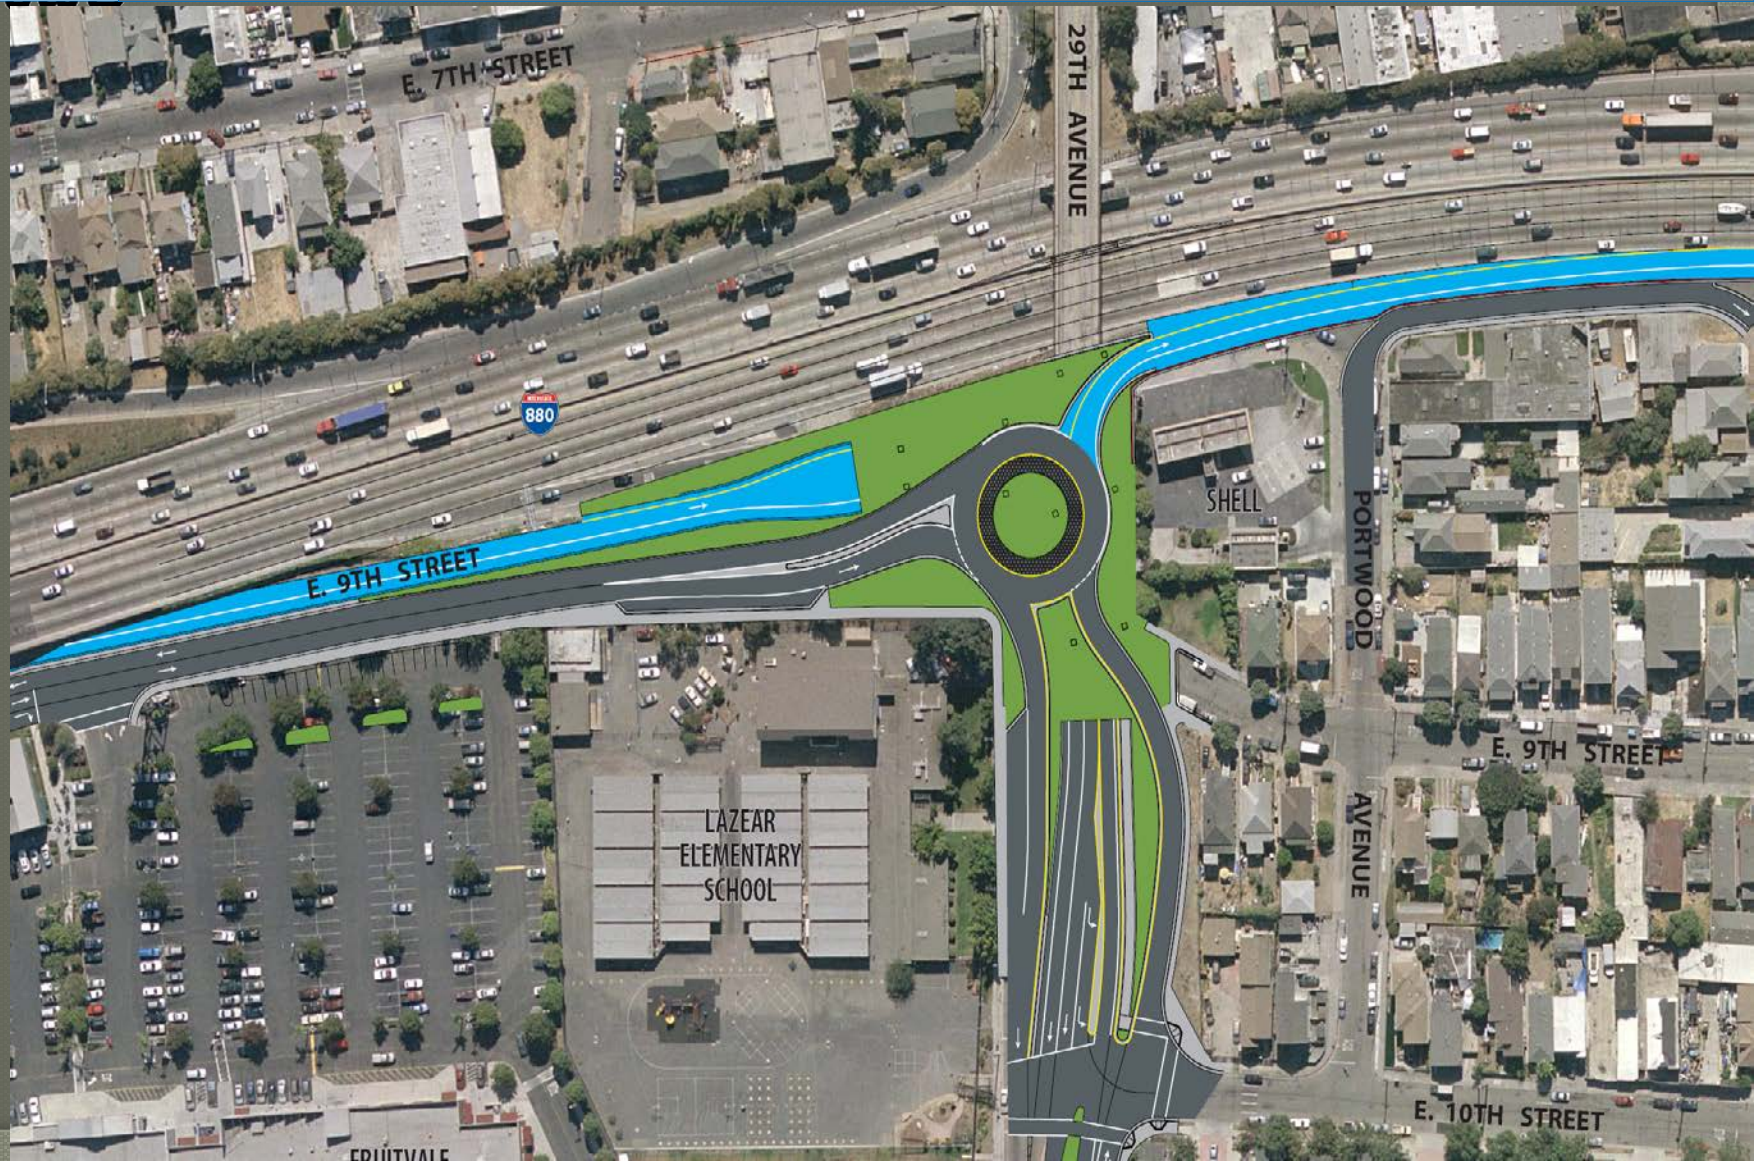

23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS






23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS






23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

Stage 4
June 2017 to
October 2018

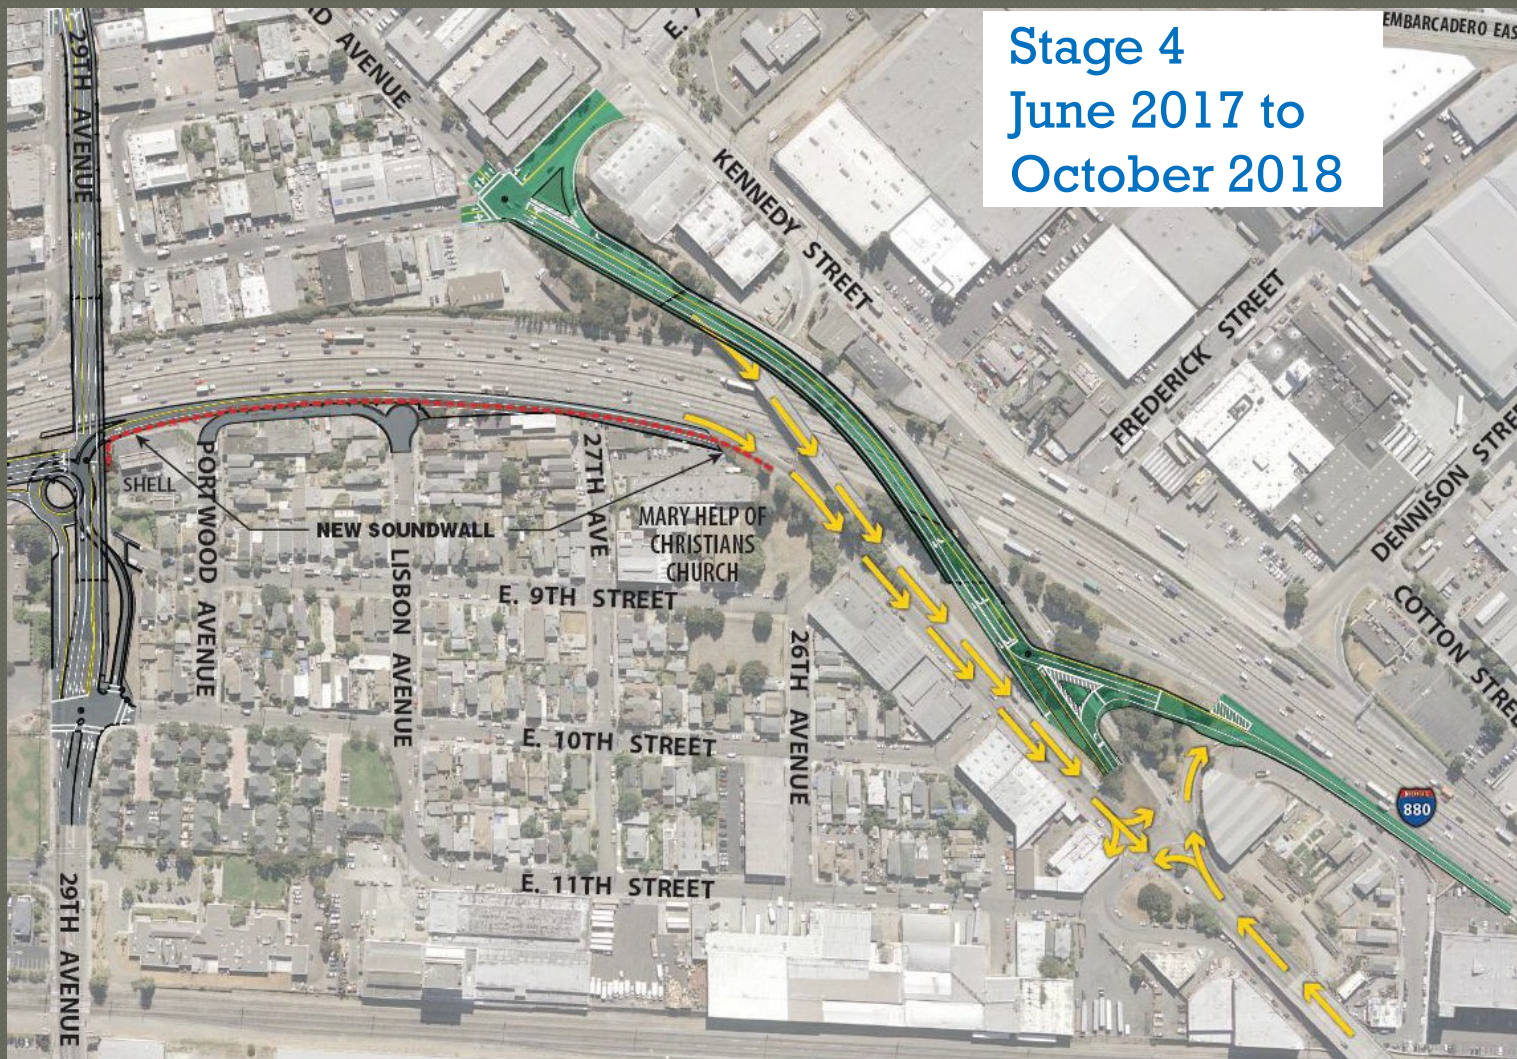

23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

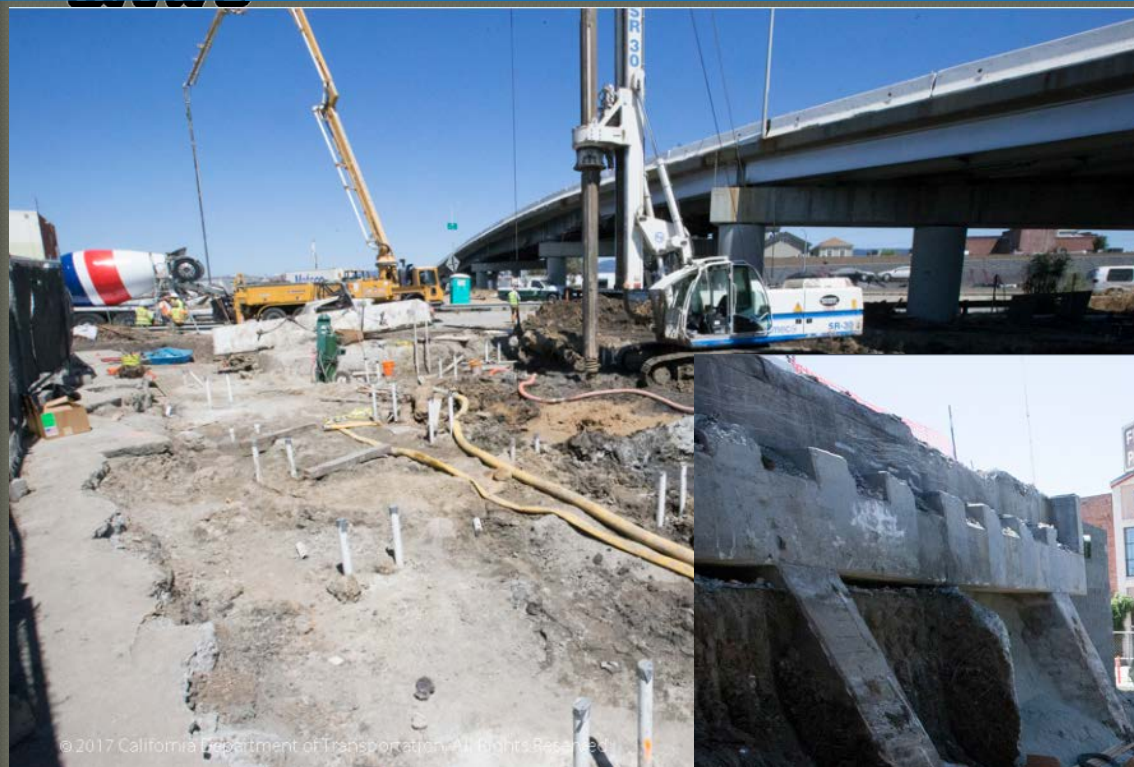



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS





23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS






23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS


- Northbound 880/23rd Ave. Onramp – 2 Weeks Closure

September 28, 2018 to October 15, 2018

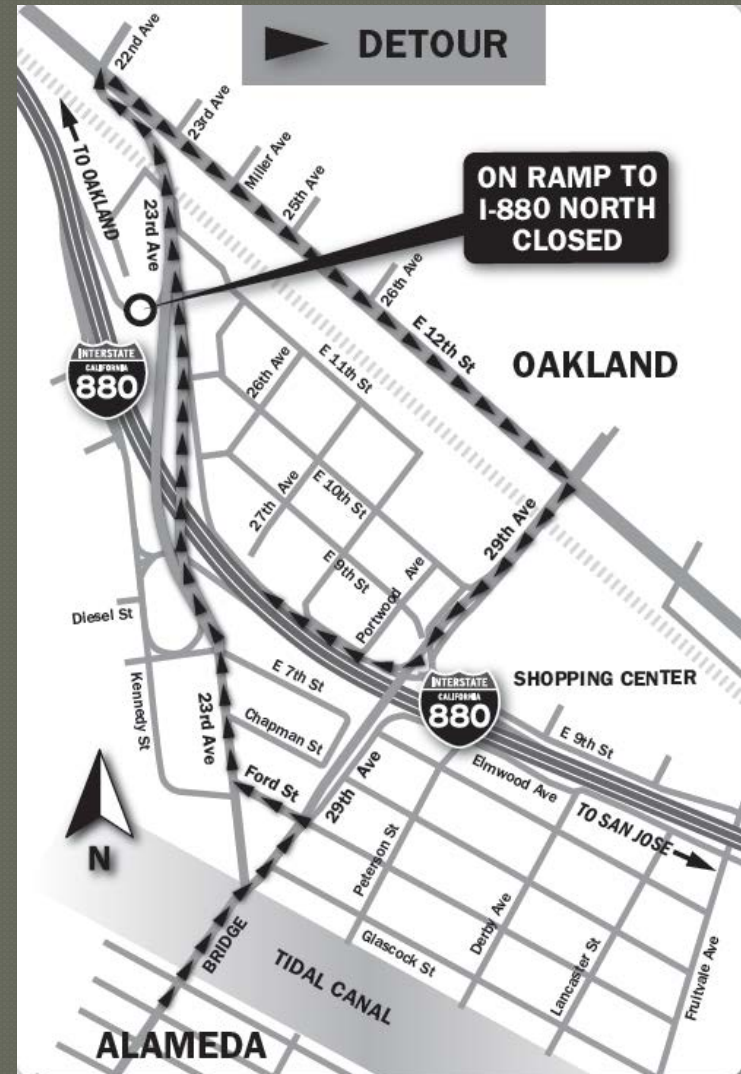



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

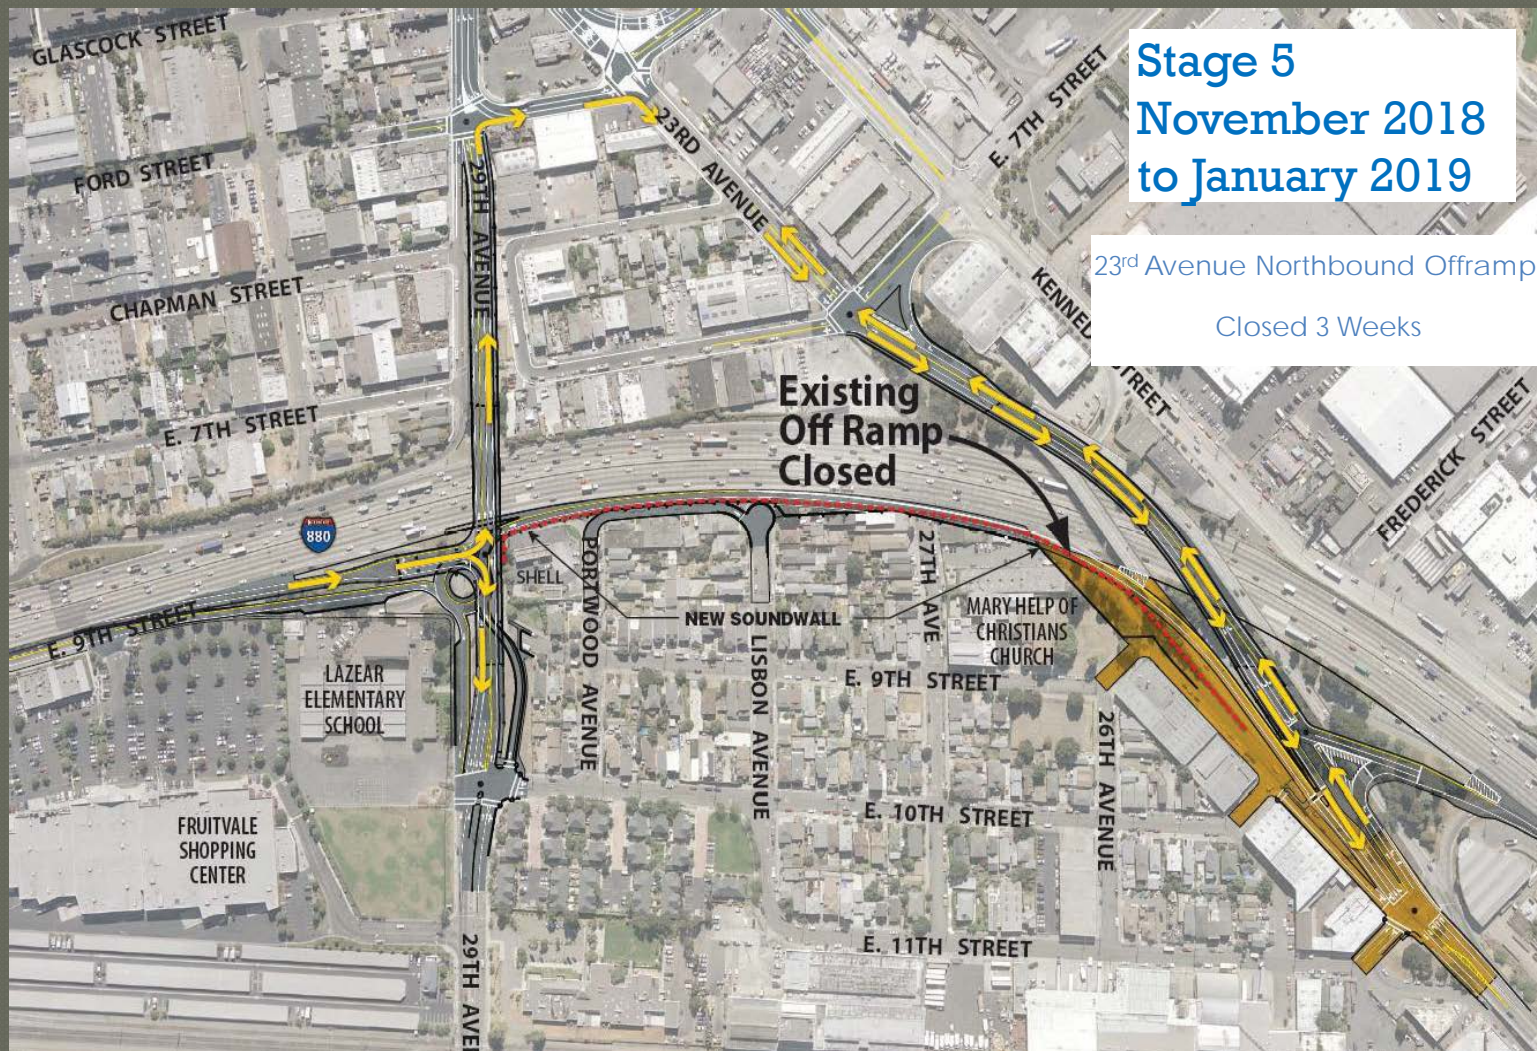

Stage 5
November 2018
to January 2019

23rd Avenue Northbound Offramp
Closed 3 Weeks




23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

- Northbound 880/23rd Ave. Offramp – 3 Weeks Closure
Beginning of December 2018

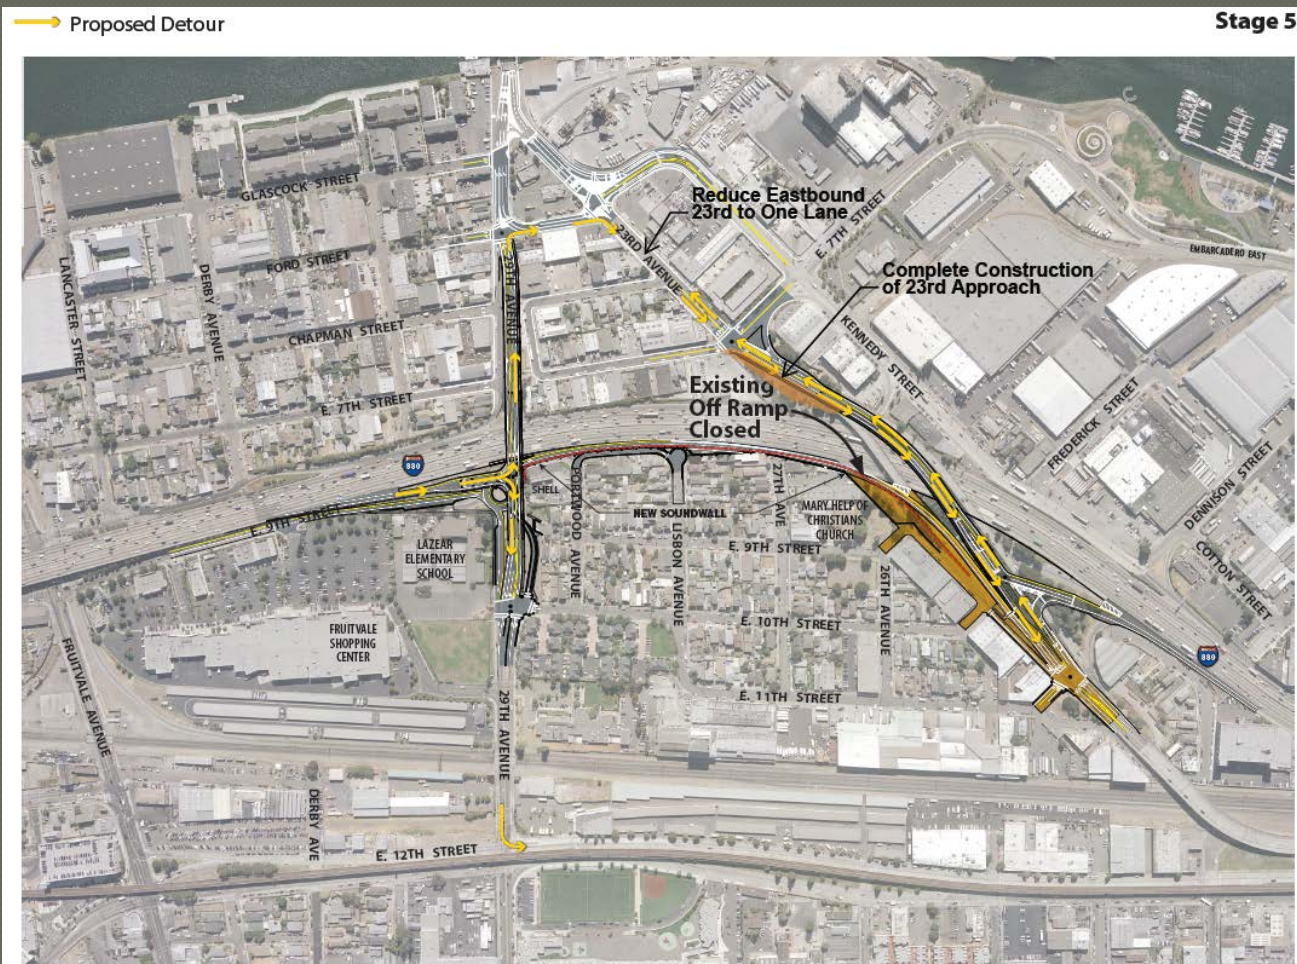



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS

- Northbound 880/23rd Ave. Onramp – 2 Weeks Closure
September 28, 2018 to October 15, 2018
- New 23rd Ave. Overcrossing – Opening mid/late October 2018
- Remaining 23rd Ave. Bridge Demolition – Beginning of November 2018
- 29th Ave. Offramp Bridge from NB 880 – Opening in November 2018
- Northbound 880/23rd Ave. Offramp – Closing for 3 weeks – Beginning of December 2018
- New Northbound 880/23rd Offramp – Opening January 2019



23RD & 29TH AVENUE OC OPERATION AND SAFETY IMPROVEMENTS



I-880 Operational and Safety Improvements at 29th Avenue and 23rd Avenue Overcrossings

